सत्यमेव जयते

India Semiconductor Mission
Catalyzing India's Semiconductor Ecosystem

STRATEGIC INITIATIVE
Strengthening India's Semiconductor Ecosystem

COLLABORATIVE APPROACH
Government, Industry & Academia Partnership

DATA-DRIVEN INSIGHTS
Real-time Monitoring for Better Decisions

MISSION MODE EXECUTION
Timely Delivery with Operational Excellence

ISM PROJECT MONITORING DASHBOARD

Real-time visibility. Timely execution. Strategic impact.



ABOUT THIS DASHBOARD

The ISM Project Monitoring Dashboard provides a unified view of all projects under the India Semiconductor Mission. Track progress across key dimensions including physical progress, financials, disbursements, risks, and milestones to ensure timely execution and mission success.

360° PROJECT VISIBILITY
Real-time overview across all critical project parameters

MONITOR & CONTROL
Track progress, risks, issues and ensure accountability

DATA-DRIVEN DECISIONS
Actionable insights for proactive decision making

STAKEHOLDER COLLABORATION
Aligned communication and transparency across all stakeholders

PROJECT BRIEF › | PHYSICAL PROGRESS › | DISBURSAL STATUS › | FINANCIAL PROGRESS › | ACTIVITY TRACKER › | MISCELLANEOUS › | PORTFOLIO INSIGHT ›

DATA AS OF : 27-Aug-26 | LAST REFRESHED : 31-Jul-26 11:51

POWERING INDIA'S SEMICONDUCTOR FUTURE

KAYNES SEMICON

Project Company

KAYNES SEMICON PRIVATE LIMITED

Shareholders

1. Text here (%)
2. Text here (%)
3. Text here (%)
4. Text here (%)

Project Cost	Eligible Capex	Incentive GOI	Incentive SG	Project Capacity	Project Co. Contribution (Debt/Equity)	Employment (Total) Direct / Indirect (M/F)

Technology & Products

1. **Wire Bond**
   [QFN, TO, SOT]
2. **Substrate Based**
   [BGA, BGA Stack Die, FC-QFN, FCBGA]
3. **Advance Packaging**
   [SIPBGA, IPM5, IPM7]

Application of end products

1. **Automobile**
2. **Defence**
3. **Aerospace**
4. **Electronics**
5. **Display**

Key Dates

1. **First chip out**
2. **Full scale commissioning**

Technology Transfer

1. **Tech Partner-01**
2. **Tech Partner-02**

On track | Risk of Delay | Delayed

Project Status



Delayed by ~5 mos.

Physical progress


Phase wise planned v/s actual

Overall progress may be provided for all projects in same view as per current dashboard

Financial progress

1. Both financial and disbursement tracker need to be linked together

(Total amount invested in project):



Outlook for next 6 months / any major update/ Update on forthcoming milestone / or any other relevant activity going to be undertaken in upcoming period.

Suppose . Any phase going to be completed or any first move in date etc

FSA Milestone tracker

FSA Milestone		
Civil Work Completion (Main Plant)	30-Jun-27	30-Jun-27
Cleanroom Construction Completion and Qualification	30-Sep-27	30-Sep-27
Utility Installation Completion (Testing and Validation)	30-Aug-27	30-Aug-27
Commercial Production for all the technologies as per the FSA definition	31-Mar-29	31-Mar-29
Equipment Installation and Qualification Completion (all lines)	30-Sep-28	30-Sep-28
First Product out for all technologies as per approval letter dated 23 SEP 2024	31-Dec-28	31-Dec-28

ILLUSTRATIVE

On track | Risk of Delay | Delayed

Project Brief module to be aligned as per the wireframe intent shared by the Client

MSTI



MSTI



CG SEMI



CG SEMI



Kaynes Semicon



Kaynes Semicon



TATA OSAT



TSMPL




SiCSem




ICPL OSAT



CSPL

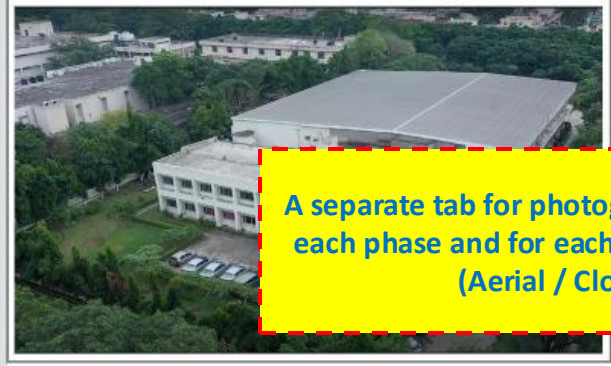

3DGS

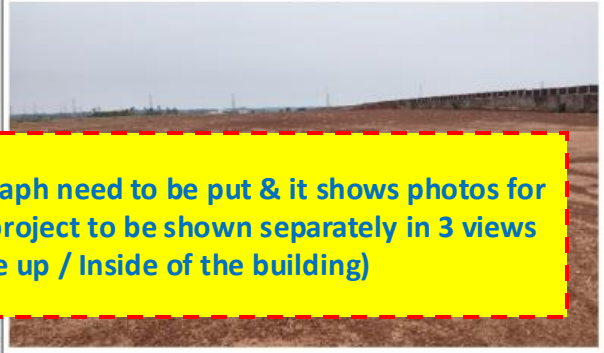


A separate tab for photograph need to be put & it shows photos for each phase and for each project to be shown separately in 3 views (Aerial / Close up / Inside of the building)

Overall Planned vs Actual Progress

Overall Actual Progress %


49.75%

Variance : -6.43%




Overall progree indicates combined progress including Main & Mini

WBS Planned vs Actual Progress & Variance %

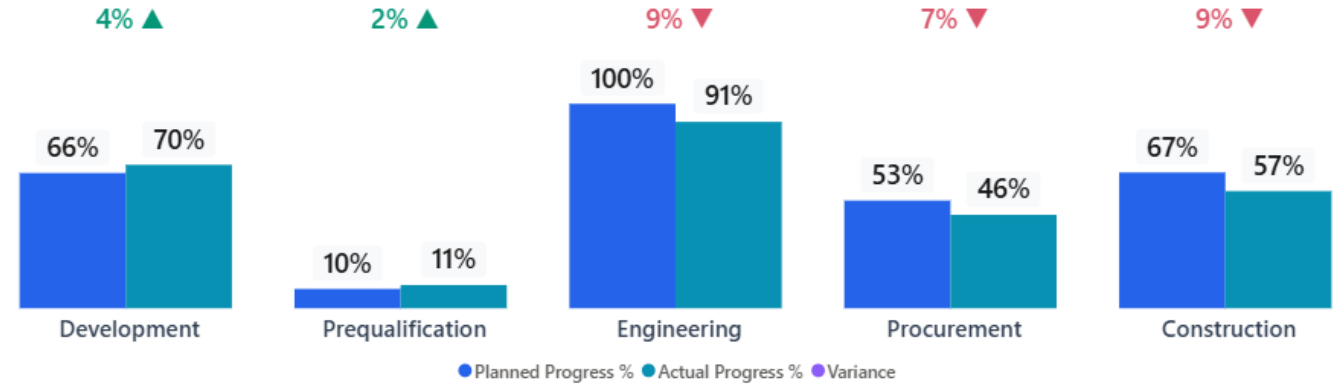


Monthly S Curve

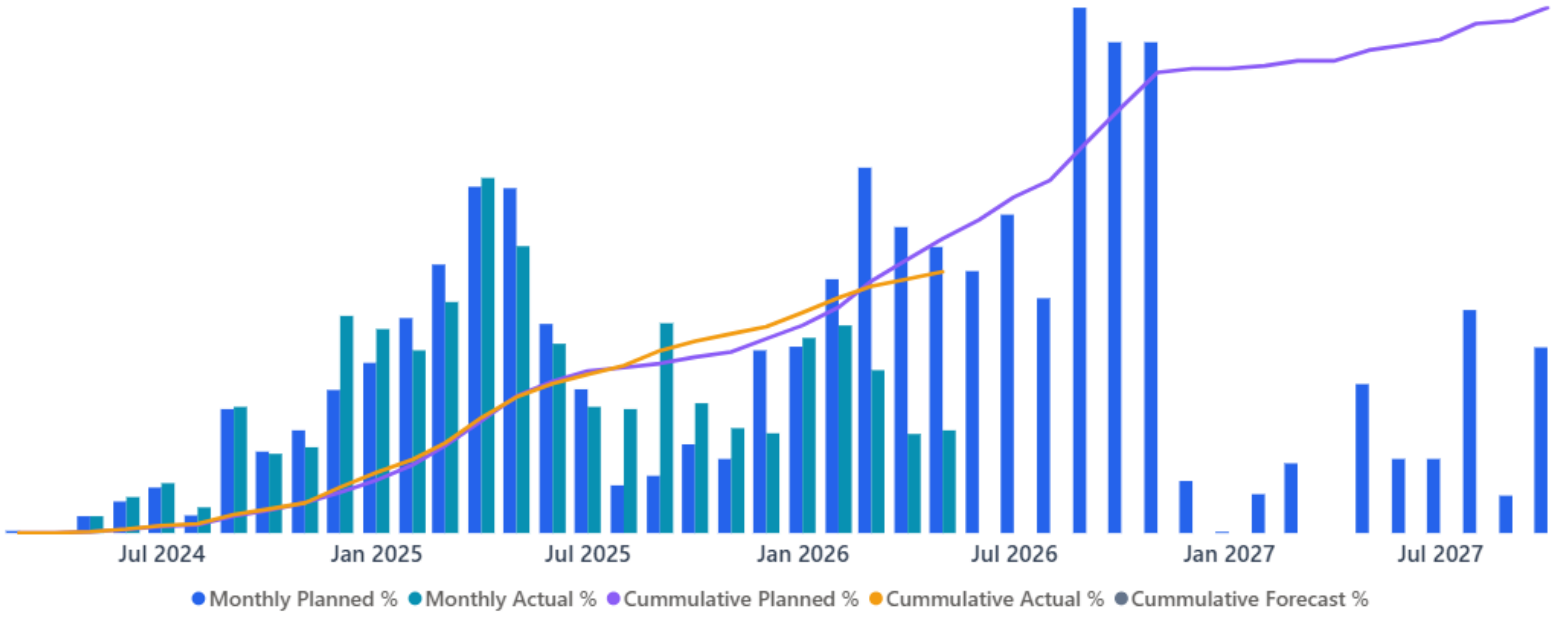

Baseline Completion : 31-Oct-27 Revised Completion by PC: (Blank) Anticipated Completion by PMC: 31-Oct-27

Building Actual Progress %

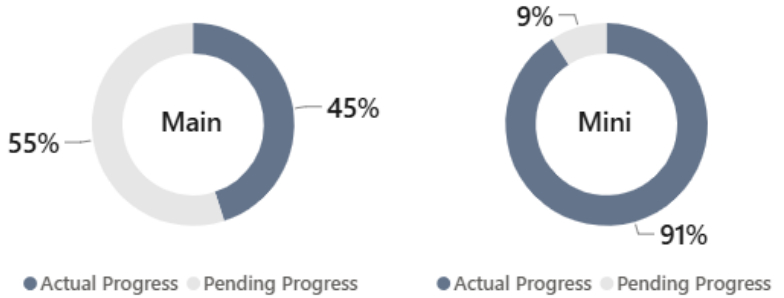


Key Consideration

- Achiveing of 31st Dec 26 Milestone is at risk for Main Plant
- Commercial production of QFP Chip begin on 4th July
- Main Plant Civil and MEP works delayed by ~4 Month

Disbursement Amount Status (INR Cr.)

Total Claim	Eligible	Approved	Requested	Disbursed
CFS 1,333 | 66%	CFS 1,144 | 63%	CFS 724 | 52%	CFS 341 | 50%	CFS 222 | 40%
RC 682 | 34%	RC 678 | 37%	RC 678 | 48%	RC 339 | 50%	RC 339 | 60%




₹ 561 Cr has been disbursed against total claims of ₹ 2,016 Cr representing 28 % of the claimed amount.

2026 | 2025 | 2024 | 2023

CFS | RC

Total Claim | Eligible | Approved | Requested | Disbursed

Quarter Wise Claim Trend (INR Cr.)

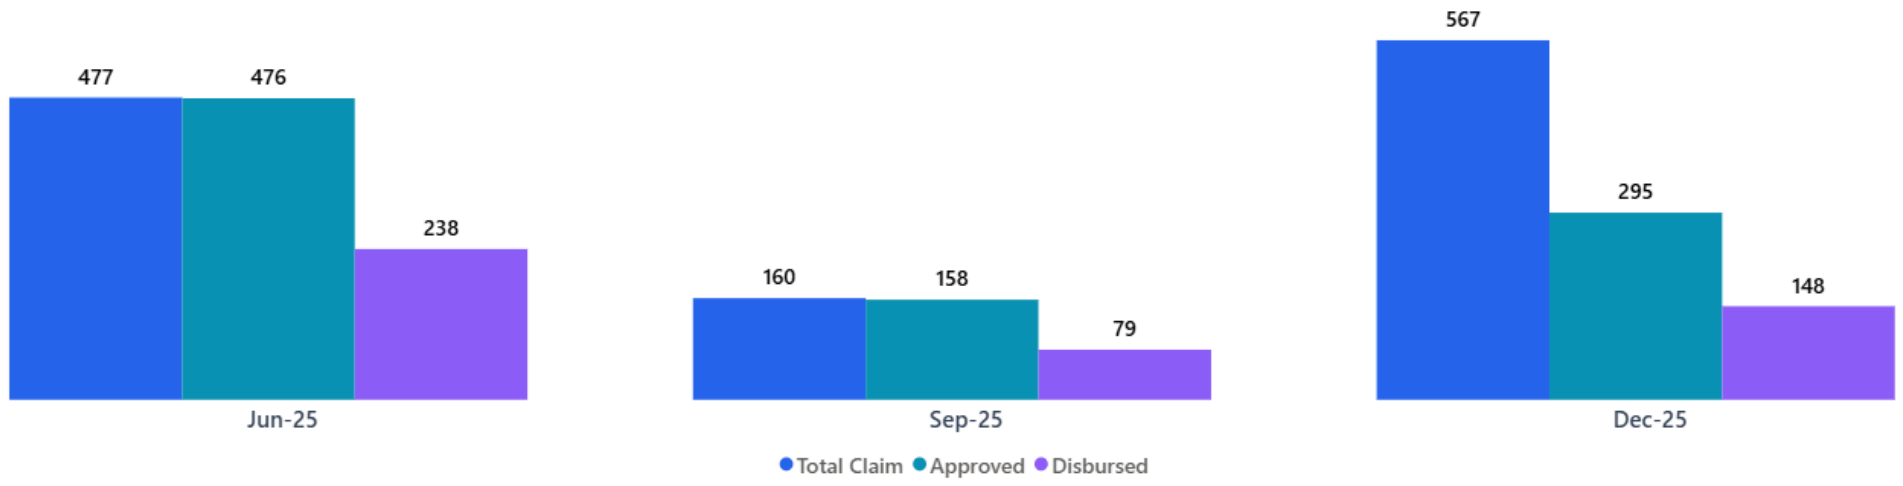

Project Cost


₹ INR Cr

7,584

Eligible	7,002
GOI	3,501
SG	769
Equity	2,481
Debt	833


ISM Share is 50% of Eligible Capex

Financial Planned vs Actual Progress




actual financial progress stands at ₹ 1,239 Cr, against a planned outlay of ₹1,504 Cr, resulting in a variance of ₹-265 Cr.

Project Cost Breakup

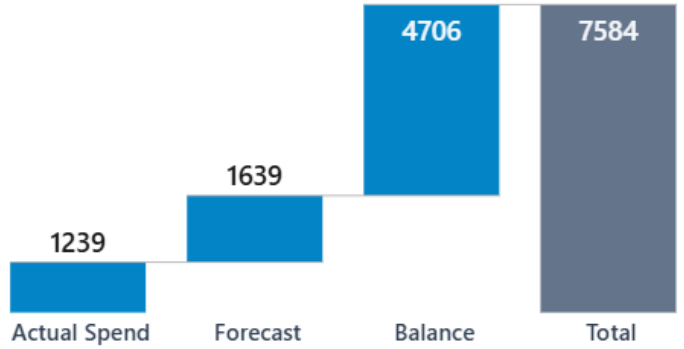


2026 | 2025 | 2024 | 2023

Quarter Wise Plan vs Actual Amount (INR Cr.)

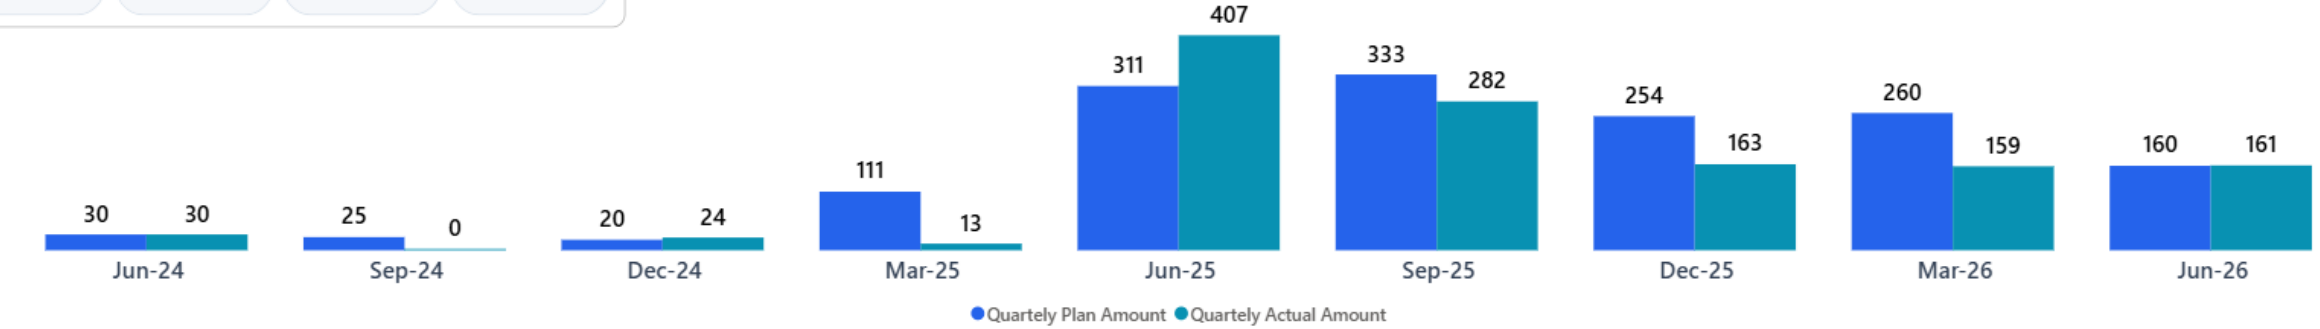

Next Quarters Forecasted Amount (INR Cr.)

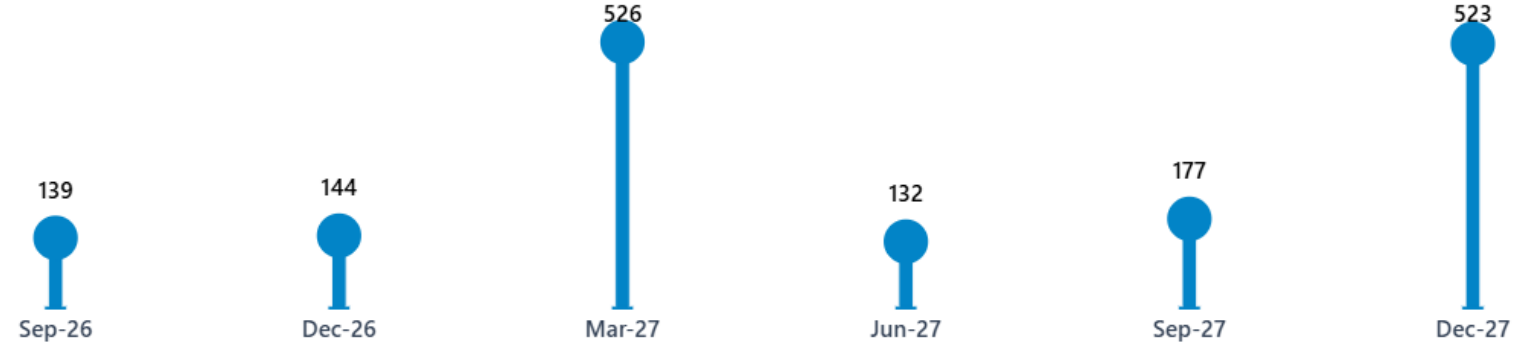

Financial Narrative

Current spending trends indicate a projected completion cost of ₹ 2,878 Cr, which remains within the approved project cost by ₹ 4,706 Cr. The projection is based on actual expenditure of ₹ 1,239 Cr and a forecasted spend of ₹ 1,639 Cr over the next forecasted quarters.

Planned Activity & FSA Milestone

WBS/Activity	Planned Completion	Forecast Completion	Remarks
⊞ FSA Milestone	31-Oct-27	31-Oct-27	At Risk
⊟ Procurement			
Pilot Plant Capex Equipment Delivery Batch 1	15-Jul-25	15-Jul-25	Completed
Pilot Plant Completion of ETP,STP,FMCS	29-Jul-25	30-Nov-25	Completed
⊟ Construction			
Main Plant Assembly Area Pre Plinth Activities	29-Sep-25	29-Sep-25	Completed
Main Plant Plating Area Civil Construction	28-Mar-26	28-Mar-26	Completed
Main Plant Plating Area Pre Plinth Activities	30-Jun-25	30-Jun-25	Completed
Main Plant Testing Area Pre Plinth Activities	24-Jul-25	24-Jul-25	Completed
Main Plant Utility Buildings Pre Plinth Activities	28-Nov-25	28-Dec-25	Completed
Pilot Plant Completion of construction of clean room & infra works	31-Jul-25	31-Jul-25	Completed
Pilot Plant Equipment Hookup Batch 1	31-Oct-25	31-Oct-25	Completed
Main Plant Engineering - LOD 350 design	28-Feb-26	28-Feb-26	In Progress
Main Plant Testing Area Civil Construction	11-Jul-26	11-Jul-26	In Progress
Pilot Plant Pre qualification and qualification activities	30-Sep-26	30-Sep-26	In Progress
Pilot Plant Equipment Hookup Batch 2	23-Jun-26	23-Jun-26	Yet to start


Total Cost

₹ INR Cr


160,355

Eligible Capex	127,113
GOI	63,555
SG	24,707
Debt	41,648
Equity	30,321


Total Cost Breakup

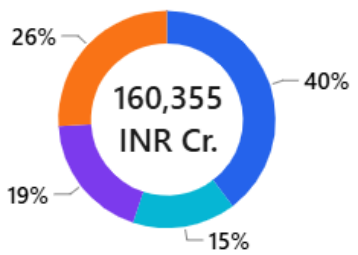


Eligible Capex Breakup

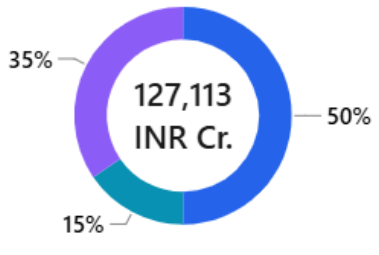


Investment Progress



Disbursement (GOI)



Disbursement Status (INR Cr.)

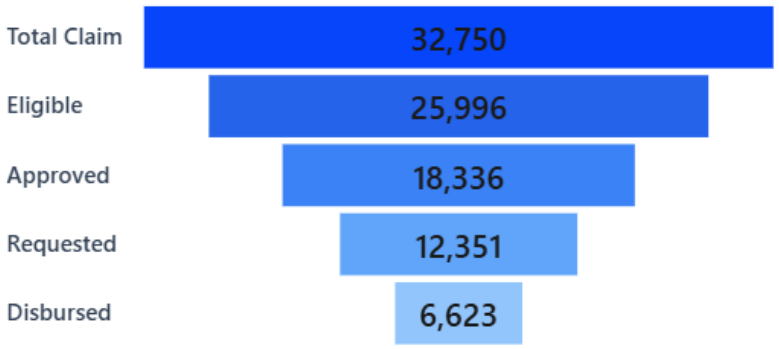

Key Consideration

- 3DGS: FSA and Transaction documents Signed.
- ASIP: Sale Deed executed on 20 May 2026
- CG: Pilot Plant commercial production started, Main plant progress has r..
- CSPL: Commercial production started; FSA aligned.
- ICPL: FSA finalized; Lease deed executed on 15 Jun 2026
- Kaynes OSAT: Pilot plant commissioned Mar-26.

Portfolio Performance Summary

Project	Type	Approval Date	Commisioning Date	Planned Progress %	Actual Progress %	Variance %
Micron ATMP	Main PH-1	15-Jun-23	15-Jun-28	100%	88%	-12%
	Main PH-2	15-Jun-23	15-Jun-28	5%	3%	-2%
	Mini	15-Jun-23	01-Jun-24	100%	100%	0%
CG OSAT	Main	08-Mar-24	30-Oct-27	45%	35%	-10%
	Mini	13-Mar-24	04-Jul-26	91%	91%	0%
Kaynes OSAT	Main Unit-2	23-Sep-24	17-Jan-27	100%	68%	-32%
	Main Unit-3	23-Sep-24	31-Oct-27	36%	0%	-36%
	Pilot Unit-1	23-Sep-24	14-Oct-25	100%	100%	0%
TATA Fab	Fab DF-1	07-Mar-24	07-Mar-30	10%	10%	-0%
TSAT	Main PH-1	07-Mar-24	31-Mar-27	84%	49%	-35%
	Main PH-2	07-Mar-24	06-Mar-29	0%	0%	0%
